ID	Task Name	Duration	Beginning	End	Predecess
1	**Progress Meetings ONR - EDF/AREVA**	**366 days**	**Tue 12/04/11**	**Wed 05/09/12**	
2	Progress Meeting 1	0 days	Tue 12/04/11	Tue 12/04/11	
3	Progress Meeting 2 (ONR feedback on Approach CAE doc)	0 days	Wed 29/06/11	Wed 29/06/11	20
4	Progress meeting 3 (intermediate CAE tables presentation)	0 days	Thu 21/07/11	Thu 21/07/11	23
5	Progress meeting 4 (intermediate CAE tables presentation)	0 days	Thu 01/09/11	Thu 01/09/11	25
6	Progress meeting 5 (Presentation of draft CAE document)	0 days	Mon 26/09/11	Mon 26/09/11	26
7	Progress meeting 6 (Teleconference clarifications ONR requests)	0 days	Mon 17/10/11	Mon 17/10/11	6
8	Progress meeting 7 (ONR feedback on draft CAE document)	0 days	Thu 20/10/11	Thu 20/10/11	27
9	Progress meeting 8 (Teleconference end workshops)	0 days	Thu 10/11/11	Thu 10/11/11	
10	HPC De Risk Meeting (ONR/NNB/EDF/AREVA - London)	0 days	Wed 29/02/12	Wed 29/02/12	30
11	Progress meeting 9 (CAE document - Montrouge)	0 days	Mon 05/03/12	Mon 05/03/12	10
12	Progress meeting 10 (CAE document - Knutsford)	0 days	Wed 04/04/12	Wed 04/04/12	31
13	Progress meeting 11 Meeting (LTR/Sep./Shedding - Montrouge)	**0 days**	**Fri 04/05/12**	**Fri 04/05/12**	32
14	NSL Level 4 meeting (+ GDA risks progress)	0 days	Tue 19/06/12	Tue 19/06/12	35
15	**Progress meeting 12 (Load shedding) to be confirmed**	**0 days**	**Wed 05/09/12**	**Wed 05/09/12**	38,39
16	**Deliverable 1 - Approach Report**	**75 days**	**Mon 14/03/11**	**Fri 24/06/11**	
17	Draft CAE tables	17 days	Mon 14/03/11	Tue 05/04/11	
18	Integration ONR feedback + creation Approach Report	42 days	Wed 13/04/11	Thu 09/06/11	2
19	**Submission to ONR**	**0 days**	**Fri 10/06/11**	**Fri 10/06/11**	
20	ONR review	10 days	Mon 13/06/11	Fri 24/06/11	19
21	**Deliverable 2 - Complete CAE Document**	**358 days**	**Wed 08/06/11**	**Fri 19/10/12**	
22	Draft CAE tables of 2nd list of claims	18 days	Wed 08/06/11	Fri 15/07/11	
23	ONR review	3 days	Mon 18/07/11	Wed 20/07/11	22
24	Draft CAE tables for 3rd list of claims	26 days	Fri 22/07/11	Fri 26/08/11	
25	ONR review	2 days	Tue 30/08/11	Wed 31/08/11	
26	Draft complete CAE Document	12 days	Fri 02/09/11	Mon 19/09/11	5
27	ONR review	19 days	Tue 20/09/11	Fri 14/10/11	26
28	Finalisation of CAE document	66 days	Fri 21/10/11	Fri 20/01/12	6,27
29	**Submission CAE document to ONR**	**0 days**	**Fri 20/01/12**	**Fri 20/01/12**	**28**
30	ONR review	27 days	Mon 23/01/12	Tue 28/02/12	29
31	Draft answers to ONR's informal comments	19 days	Tue 06/03/12	Fri 30/03/12	11
32	Formal comments from ONR (EPR7041R)	15 days	Tue 10/04/12	Mon 30/04/12	12
33	2nd update of CAE document	69 days	Tue 01/05/12	Fri 03/08/12	32
34	Additional ONR's query TQ-EPR-1617 item 1	0 days	Fri 01/06/12	Fri 01/06/12	13
35	Draft response plan to TQ-EPR-1617 item 1	12 days	Fri 01/06/12	Mon 18/06/12	34
36	Finalised response plan to TQ-EPR-1617 item 1	24 days	Tue 19/06/12	Fri 20/07/12	14
37	**Submission of updated CAE document to ONR**	**0 days**	**Fri 03/08/12**	**Fri 03/08/12**	**33**
38	ONR review	15 days	Mon 06/08/12	Fri 24/08/12	37
39	Part response to TQ-EPR-1617 item 1	28 days	Mon 23/07/12	Wed 29/08/12	36
40	**Submission of part response to TQ-EPR-1617 item 1**	**0 days**	**Wed 29/08/12**	**Wed 29/08/12**	39
41	Final response to TQ-EPR-1617	18 days	Wed 05/09/12	Fri 28/09/12	15
42	**Submission of Final response to TQ-EPR-1617**	**0 days**	**Fri 28/09/12**	**Fri 28/09/12**	41
43	Final update of the CAE document	40 days	Mon 27/08/12	Fri 19/10/12	38
44	**Submission of final update of the CAE document**	**0 days**	**Fri 19/10/12**	**Fri 19/10/12**	43
45	**Deliverable 3 - Update of PCSR Sub-chapters 8.1 to 8.6**	**232 days**	**Thu 01/12/11**	**Fri 19/10/12**	
46	Advanced updates of sub-chapters	56 days	Thu 01/12/11	Thu 16/02/12	27
47	**Submission of advance updates to ONR**	**0 days**	**Thu 16/02/12**	**Thu 16/02/12**	**46**
48	ONR review	55 days	Fri 17/02/12	Thu 03/05/12	47
49	Updates of sub-chapters	64 days	Tue 08/05/12	Fri 03/08/12	13
50	**Submission updated PCSR Sub-chapter(s)**	**0 days**	**Fri 03/08/12**	**Fri 03/08/12**	**49**
51	ONR review	22 days	Mon 06/08/12	Tue 04/09/12	50
52	Final updates of sub-chapters impacted by TQ-EPR-1617 item 1	33 days	Wed 05/09/12	Fri 19/10/12	15
53	**Submission of final updates of sub-chapters**	**0 days**	**Fri 19/10/12**	**Fri 19/10/12**	52

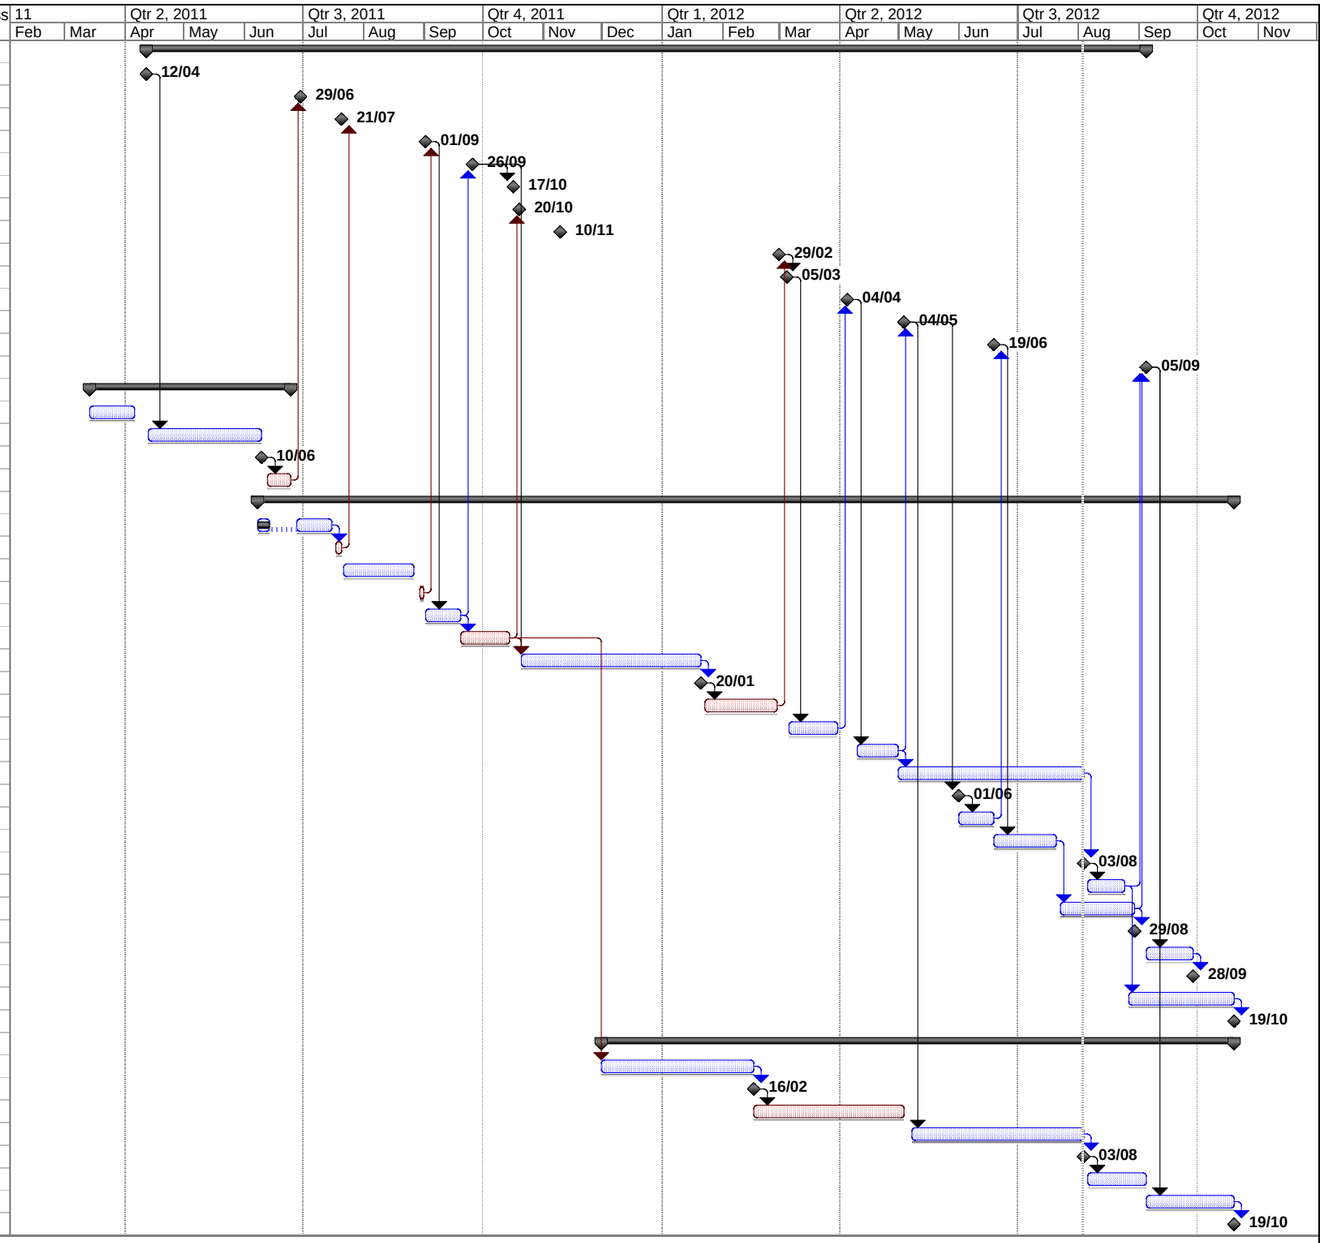

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
