ID	Task Name	Duration	Start	Finish
1	**Action 1 of GI-UKEPR-RC02**	**370 days**	**Mon 02/05/11**	**Fri 28/09/12**
2	**Task 1 - UK EPR Activity Estimation and Characterization**	**299 days**	**Mon 02/05/11**	**Thu 21/06/12**
3	Draft Table of Contents Issued to ONR	0 days	Fri 17/06/11	Fri 17/06/11
4	Report and Analysis Preparation	45 days	Mon 02/05/11	Fri 01/07/11
5	Project Validation	5 days	Mon 04/07/11	Fri 08/07/11
6	Issuance to ONR	0 days	Fri 08/07/11	Fri 08/07/11
7	Meeting 1 - Discussion on report and Prel comments	0 days	Thu 29/09/11	Thu 29/09/11
8	TSC Review	54 days	Mon 09/04/12	Thu 21/06/12
9	ONR Assessment and validation	110 days	Mon 11/07/11	Fri 15/06/12
10	**Task 2 - UK EPR Auxiliary Systems Activity Estimation and Monitoring**	**336 days**	**Fri 17/06/11**	**Fri 28/09/12**
11	Draft Table of Contents Issued to ONR	0 days	Fri 17/06/11	Fri 17/06/11
12	Report and Analysis Preparation	105 days	Wed 11/01/12	Tue 05/06/12
13	Project Validation	3 days	Wed 06/06/12	Fri 08/06/12
14	Meeting 2 - Presentation of task 2 report	0 days	Tue 22/05/12	Tue 22/05/12
15	Issuance to ONR	0 days	Fri 08/06/12	Fri 08/06/12
16	TSC Review	40 days	Mon 11/06/12	Fri 03/08/12
17	ONR Assessment	40 days	Mon 11/06/12	Fri 03/08/12
18	Resolution of ONR Assessment Comments (if applicable)	35 days	Mon 06/08/12	Fri 21/09/12
19	project validation of Updated Documentation (if applicable)	5 days	Mon 24/09/12	Fri 28/09/12
20	Issuance to ONR	0 days	Fri 28/09/12	Fri 28/09/12
21	**Task 3 - PCSR Update - Sub-chapter 5.5**	**228 days**	**Thu 13/10/11**	**Mon 27/08/12**
22	PCSR Update Preparation (Advance Version)	30 days	Thu 13/10/11	Wed 23/11/11
23	Project Validation	5 days	Thu 24/11/11	Wed 30/11/11
24	Issuance to ONR (Actual Issue Date)	0 days	Wed 30/11/11	Wed 30/11/11
25	ONR Assessment	22 days	Thu 01/12/11	Fri 30/12/11
26	PCSR Update preparation (Final version)	41 days	Fri 20/04/12	Fri 15/06/12
27	Project Validation	6 days	Mon 18/06/12	Mon 25/06/12
28	Issuance to ONR	0 days	Mon 25/06/12	Mon 25/06/12
29	ONR Assessment	25 days	Tue 26/06/12	Mon 30/07/12
30	Resolution of ONR Assessment Comments (if applicable)	15 days	Tue 31/07/12	Mon 20/08/12
31	Project validation of Updated Documentation (if applicable)	5 days	Tue 21/08/12	Mon 27/08/12
32	Issuance to ONR	0 days	Mon 27/08/12	Mon 27/08/12

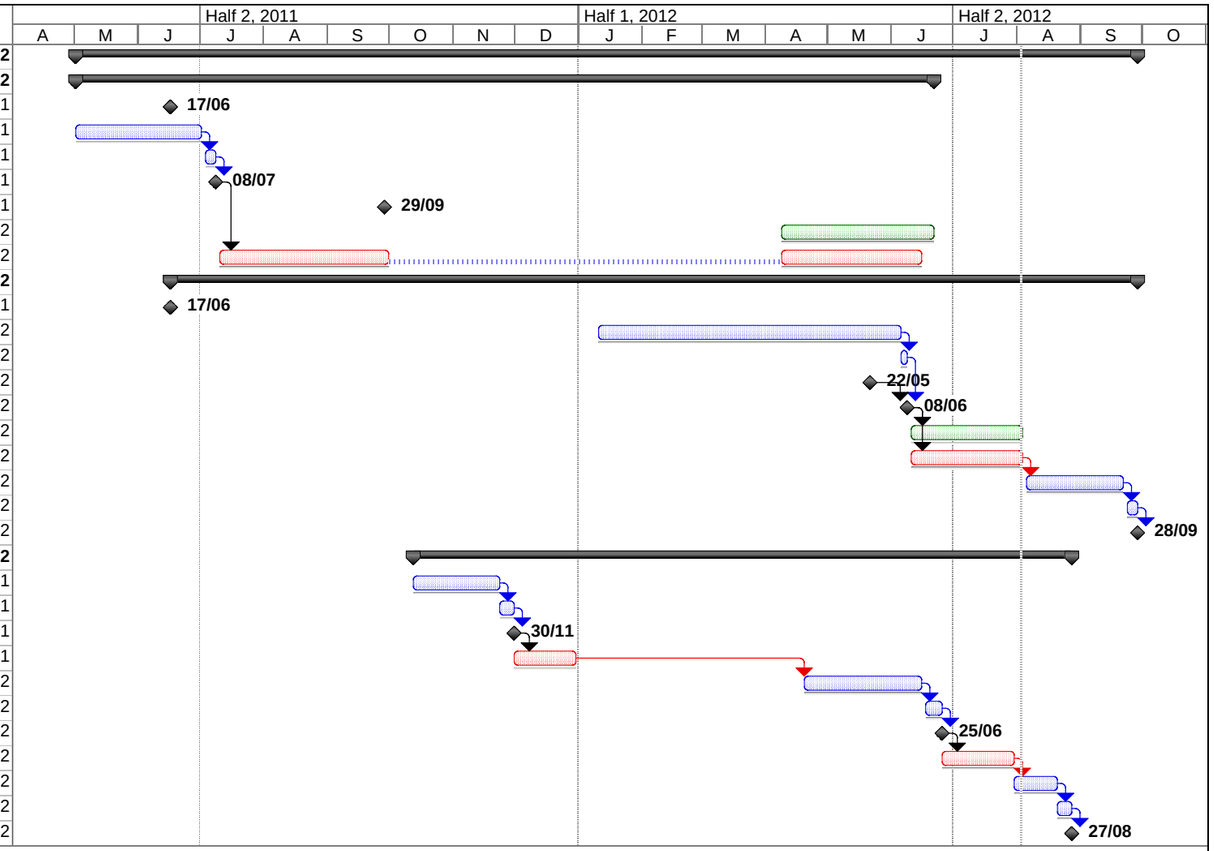

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
